

ESTIMATION REPORT

TWO STOREY



THIS IS AN EXAMPLE REPORT, PRICES MAY NOT REFLECT MARKET PRICES

Client Name: Example Client
Address: Cavan

Email: client@gmail.com
Tel No: +353 7123456789

Architect: Example Architectural Design
Email: info@examplearchitecture.com
Tel No: +353 789456123

Self Build--Sliver package

105

New Build

DJ Build Estimations – 41 Kingarow Road – Derrylin – Co Fermanagh – BT92 9HZ

Tel: 02867742016 Mob: 07771935887

Email: info@djestimations.com

Copyright © 2017, DJ Estimations

Guidance Notes

Labour prices will be for guidance only. We will estimate labour rates for your area to the best of our knowledge. There will always be price variations, but it is the timeframe that we are promoting accuracy for.

Hired in digger does NOT include Driver Labour
13 -20 Ton digger rates generally do include driver labour/owner driver

Delivery charges of plant will depend on distance from supplier

Please note foundation price is presumed on good ground conditions. If ground conditions are poor, this will incur additional costs for possibly piling or steel mesh reinforcement.

Before foundations or ring beam is poured: inspection approval by building control (UK only), or an architect or engineer (ROI) is needed

Material costs are based on the average for your area

Overslab is inclusive of the following tasks: Backfill Substructure with aggregates, first fixture of drainage pipes & services, radon barrier, steel mesh (if required) and pour of concrete subfloor

PC SUMS is a presumed cost for Electrical, Plumbing, Kitchen, Stairs & Sanitary ware etc

In plant and labour, 8 hours is generally described or equal to 1 working day

General housekeeping relates to clean up and removal of waste at each phase

If you engaging contractor please allow for their Prelims/overheads & Profit!

VAT to be added if applicable. Prices will be Net



Preliminaries

Item	Description	Qty	Cost per week	Projected time on site	Total Cost
Item 1	Site Huts/welfare	1	€38.00	44	€1,672.00
	Delivery/collection	1	€200.00	1	€200.00
Item 3	Toilets/serviced	1	€35.00	44	€1,540.00
	Delivery/collection	1	€200.00	1	€200.00
Item 4	Water Supply (temporary one off cost)	1	€350.00	1	€350.00
Item 5	Electricity Connections (temporary one off cost)	1	€1,200.00	1	€1,200.00
Item 6	Site Security/optional Allowance	1	€500.00	1	€500.00
Item 7	Hoarding	1	€250.00	1	€250.00
Item 8	Skips & Recycling /general/6/8yrd	6	€350.00	1	€2,100.00
Item 9	Scaffolding Hire, Erect,Alter & Dismantel store	1	€7,000.00	1	€7,000.00
Item 10	Insurances	1	€2,000.00	1	€2,000.00

The above costs are the clients discretion to alter or remove to suit their own requirements

Total €17,012.00

Client	Example Client	New Build
---------------	-----------------------	------------------

**Build Phase - Site Clearance / Access****Material**

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Stone / Aggregate	Crusher Run	4"	60	Tonne	€14.00	€840.00
Stone / Aggregate	Crusher Run	2"	140	Tonne	€14.00	€1,960.00
Stone / Aggregate	Drainage Stone	3/4"	20	Tonne	€15.00	€300.00
Stone / Aggregate	Blinding	1/2"	140	Tonne	€15.00	€2,100.00
Stone / Aggregate	Dust	specific	20	Tonne	€16.00	€320.00
PVC Drainage Pipe		150mm	2	No.	€22.00	€44.00
Consumables - Allowance	Lines		1		€25.00	€25.00
Consumables - Allowance	Spray marker		1		€25.00	€25.00
Ground Support Terram - Access Lane Prov		4.5x100m	1	Roll	€245.00	€245.00
Fixings & supports - Allowance			1		€100.00	€100.00

Material Total	€5,959.00
-----------------------	------------------

Plant

Plant Needed	Hours/QTY	Hired off	Rate Per day	Rate per Hour/QTY	Fuel Cost	Total
13 Tonne Digger - Strip topsoil	12	INC DRIVER & FUEL		€60.00		€720.00
13 Tonne Digger - Form Access lane	8	INC DRIVER & FUEL		€60.00		€480.00
13 Tonne Digger - Reduce dig to form raft	12	INC DRIVER & FUEL		€60.00		€720.00
13 Tonne Digger - form raft build up	12	INC DRIVER & FUEL		€60.00		€720.00
Dumper 9T- Strip Topsoil/Form Access Lane	20			€13.00	€100.00	€360.00
80cm Tandem Roller	16			€6.50	€50.00	€154.00
Delivery Charges	1			€200.00		€200.00

Plant Total	€3,354.00
--------------------	------------------

Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Line out site	2	3		€30.00		€180.00
Create access lane with digger in plant	1	0.1		€2.00		€0.10
Dumper to access lane driver	1	20		€30.00		€600.00
Reduced dig - in plant	1	0.5		€0.50		€0.13
Clear topsoil with digger - in plant	1	0.5		€0.50		€0.13
Remove topsoil with dumper - in plant	1	0.5		€0.50		€0.13
Form stone buildup/raft	2	16		€30.00		€960.00
Housekeeping	1	1		€30.00		€30.00

Labour Total	€1,770.48
---------------------	------------------

Assumptions:

- We are assuming all clay from reduced dig and foundations to be removed from site
- We are allowing a stone buildup for underneath raft for maximum of 500mm, this will be determined by actual ground conditions and may need to be adjusted.

Material	€5,959.00
Plant	€3,354.00
Labour	€1,770.48
Phase Total	€11,083.48



Client**Example Client****New Build****Build Phase - Foundations** Raft Foundation**Material**

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Pipes	Sewer Pipe	4"	5	lengths	€27.00	€135.00
Pipe Fittings	Medium range 90's		2	number	€10.00	€20.00
Pipe Fittings	Top hats		8	number	€9.00	€72.00
Pipe Fittings	T/Y's/45/30/15	Allowance	1	number	€100.00	€100.00
Pipe Fittings	Long range 90		1	number	€28.00	€28.00
Concrete	35N		100	Mc3	€112.00	€11,200.00
Steel Mesh	A393	4.8 x 2.4	20	Sheets	€71.00	€1,420.00
Radon Sump			1	number	€37.00	€37.00
Radon Joint Tape		3x30m	5	number	€15.10	€75.50
Radon Barrier	Visqueen Gas Resistant S/A Membrane	4x20m	4	Rolls	€310.50	€1,242.00
Timber/Profiles	(general allowance)		1		€30.00	€30.00
Consumables	Marker spray		1		€30.00	€30.00
Consumables	Lines/Nails		1		€25.00	€25.00
Steel Rebar (Quotes Attached)		12mm	2.1	tonne	€1,000.00	€2,100.00
Delivery of steel			1		€700.00	€700.00
OSB Board Shuttering 22mm			10	sheets	€33.00	€330.00
Timber shuttering supports		2x2	100	metres	€0.95	€95.00

Material Total €17,504.50**Plant**

Plant Needed	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
13 Tonne Digger - form & pour founds	12	INC DRIVER & FUEL		€55.00		€660.00
Telehandler	8			€16.00	€30.00	€158.00
Concrete Poker	8			€5.00	€10.00	€50.00
Delivery Charges	1			€150.00		€150.00


Plant Total €1,018.00**Labour**

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Line out founds	2	5		€30.00		€300.00
Driving digger in plant	1	0.5		€0.50		€0.13
Driving tractor & dump in plant	1	0.5		€0.50		€0.13
Steel cages, rebar, mesh etc fitted	2	16		€30.00		€960.00
Form concrete shuttering to raft	2	16		€30.00		€960.00
Fit services & drainage	2	8		€30.00		€480.00
Pour raft foundations	2	12		€30.00		€720.00
Housekeeping	1	3		€30.00		€90.00

Labour Total €3,510.25**Assumptions:**

- Overslab and foundation raft costed together as this is constructed in tandem.

Material	€17,504.50
Plant	€1,018.00
Labour	€3,510.25
Phase Total	€22,032.75

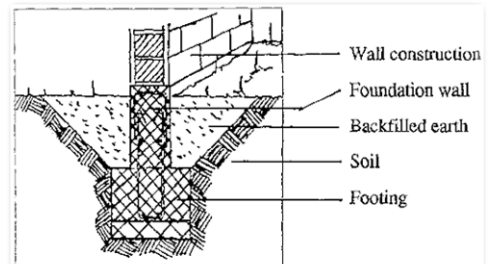



Client

Example Client

New Build

Build Phase - Substructure / Footings

Materials

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Blocks to external walls	4" Block on edge	215mm	440	Number of	€0.65	€286.00
Soap Bars	4x4		30	Number of	€0.65	€19.50
Thermal Blocks Cavity Wall	4" Thermal block on edge		120	Number of	€2.60	€312.00
Thermal Blocks Cavity Wall	4" Thermal block on flat		280	Number of	€2.60	€728.00
Thermal Blocks Internal Wall	4" Thermal block on edge		110	Number of	€2.60	€286.00
Thermal Blocks Internal Wall	4" Thermal block on flat		25	Number of	€2.60	€65.00
Sand	Building Sand		3.5	Tonne	€57.50	€201.25
Cement	Portland Cement	25kg	35	Bags	€6.60	€231.00
Mortar Mix			1	Number of	€16.00	€16.00
Damp Proof Course	Visqueen Zedex CPT	1m x 20m	5	Rolls	€90.00	€450.00

Materials Total	€2,594.75
-----------------	-----------

Plant

Plant Needed	Hours/QTY	Hired off	Rate Per day	Rate per Hour/QTY	Fuel Cost	Total
Mixer	8			€1.50	€10.00	€22.00
Telehandler	8			€15.00	€20.00	€140.00
Delivery charges	1			€100.00		€100.00

Plant Total	€262.00
-------------	---------

Labour


Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Setting out profiles	2	2		€30.00		€120.00
Build substructure/footings to DPC Level	3	12		€30.00		€1,080.00
General housekeeping	1	2		€30.00		€60.00

Labour Total	€1,260.00
--------------	-----------

Assumptions:

- To DPC level inc thermal blocks.

Material	€2,594.75
Plant	€262.00
Labour	€1,260.00
Phase Total	€4,116.75

TYPES OF FOUNDATION
 Major Building Parts


Client	Example Client	New Build
---------------	-----------------------	------------------

**Build Phase - Overslab****Raft build up****Material**

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Stone / Aggregate	Crusher Run	2"	30	Tonne	€13.00	€390.00
Stone / Aggregate	Drainage Stone	4"	100	Tonne	€13.00	€1,300.00
Stone / Aggregate	Blinding	1/2"	15	Tonne	€13.50	€202.50
Stone / Aggregate	Dust	specific	15	Tonne	€14.00	€210.00
Consumables			1		€20.00	€20.00
Other Materials			1		€50.00	€50.00

Materials Total	€2,172.50
------------------------	------------------

Plant

Plant Needed	Hours/QTY	Hired off	Rate Per day	Rate per Hour/QTY	Fuel Cost	Total
13 Tonne digger	16	INC DRIVER & FUEL		€60.00		€960.00
Dumper 6T	8			€9.00	€35.00	€107.00
Whackerplate	16			€3.00	€20.00	€68.00
Kango/small plant	1			€50.00	€20.00	€70.00

Plant Total	€1,205.00
--------------------	------------------

Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Prep & backfill aggregate	2	8		€25.00		€400.00
Housekeeping	1	2		€25.00		€50.00

Labour Total	€450.00
---------------------	----------------

Assumptions:

- Please note concrete for raft is in foundation phase !!**

Material	€2,172.50
Plant	€1,205.00
Labour	€450.00
Phase Total	€3,827.50

Client	Example Client	New Build
---------------	-----------------------	------------------

**Build Phase - Superstructure****Material**

Type of Material	Description/Area	Size	Quantity	Unit of Meas	Cost per Unit	Total
Blocks Cavity Walls	4" on edge/ Main walls	100mm	8400	No.	€0.74	€6,216.00
Blocks Cavity Walls	4" on flat / Main walls	215mm	3350	No.	€0.74	€2,479.00
Blocks Internal Walls	4" on edge	100mm	2900	No.	€0.74	€2,146.00
Blocks Internal Walls	4" on flat	215mm	400	No.	€0.74	€296.00
Soap Bars	4x4		250	No.	€0.78	€195.00
Soap Bars	6x4		600	No.	€0.78	€468.00
Bricks	Con. Brick		800	No.	€0.39	€312.00
Built in stone	natural		150	m2	€45.00	€6,750.00
Sand	To blockwork		40	Tonne	€57.50	€2,300.00
Sand	To stonework		16	Tonne	€57.50	€920.00
Cement	To blockwork	25kg	200	Bags	€6.60	€1,320.00
Cement	To stonework	25kg	130	Bags	€6.60	€858.00
Mortar Mix			4	Number of	€15.00	€60.00
Wall Starter Kit			1	No.	€22.50	€22.50
Wall Ties	Standard	250mm	4	box of 250	€30.00	€120.00
DPC's	30m roll	4"-100mm	3	Rolls	€2.95	€8.85
DPC's	30m roll	6"-150mm	6	Rolls	€4.40	€26.40
DPC's	30m roll	9"-220mm	6	Rolls	€6.50	€39.00
DPC's	30m roll	12"-337.5mm	4	Rolls	€9.75	€39.00
DPC's	30m roll	18" -450mm	3	Rolls	€13.00	€39.00
DPC's	30m roll	24" - 600mm	3	Rolls	€17.40	€52.20
Insulation	Built in	140mm	100	bales	€86.00	€8,600.00
Prop Cavity Closer	150mm wide	2.4m length	71	No.	€9.00	€639.00
Deep Face Cill 90-100mm	Ground floor	3' - 900mm	2	No.	€17.00	€34.00
Deep Face Cill 90-100mm	Ground floor	4' - 1200mm	4	No.	€22.00	€88.00
Deep Face Cill 90-100mm	Ground floor	5' - 1500mm	3	No.	€27.50	€82.50
Deep Face Cill 90-100mm	Ground floor	7'-2100mm	1	No.	€48.20	€48.20
Deep Face Cill 90-100mm	First Floor	3' - 900mm	1	No.	€17.00	€17.00
Deep Face Cill 90-100mm	First Floor	4' - 1200mm	7	No.	€22.00	€154.00
Deep Face Cill 90-100mm	First Floor	5' - 1500mm	1	No.	€27.50	€27.50
Lintels 150x100mm	Ground floor	3' ⁶ - 1050mm	10	No.	€7.30	€73.00
Lintels 150x100mm	Ground floor	4' ⁶ - 1350mm	30	No.	€9.35	€280.50
Lintels 150x100mm	Ground floor	5' - 1500mm	6	No.	€13.40	€80.40
Lintels 150x100mm	Ground floor	5' ⁶ - 1650mm	6	No.	€14.75	€88.50
Lintels 150x100mm	Ground floor	6' - 1800mm	2	No.	€12.50	€25.00
Lintels 215x 100mm	Ground floor	7' ⁶ - 2250mm	4	No.	€36.60	€146.40
Lintels 215x 100mm	Ground floor	8' ⁶ - 2650mm	2	No.	€43.08	€86.16
Lintels 215x 100mm	First Floor	6' - 1800mm	4	No.	€29.25	€117.00
Keystone Lintels	as per quote		1		€1,300.00	€1,300.00
Steel RSJ x1 No	Kitchen	203x133x30UB	3.6	m	€36.00	€129.60
Steel RSJ	Sitting Room	203x203x30UB	2.2	m	€45.00	€99.00
Steel RSJ	Porch	203x203x30UB	2.4	m	€45.00	€108.00
Steel Allowance			1		€450.00	€450.00
Padstones	6x4	1.2	4		€10.00	€40.00
Pre-stress flooring slab	Quote Attached	6"	105	m2	€57.00	€5,985.00
Pre-stress flooring grout	1.5m fine mix 30N		1.2	m3	€110.00	€132.00
Chimey finishes PC SUM	Dummy Chimney	700mm x 900mm	2	No.	€450.00	€900.00
Chimey finishes	Bird cage		2	No.	€40.00	€80.00
Lead Rolls	6m rolls	9"	3	Rolls	€101.00	€303.00
Starter Trays Porch	Wall to roof abudment porch	6 per metre	2	No.	€8.50	€17.00
Apex Trays Porch	Wall to roof abudment porch	6 per metre	1	No.	€17.50	€17.50
Cavity Trays Porch	Wall to roof abudment porch	6 per metre	26	No.	€8.50	€221.00
Expanding Metal	100mm x 20m		3	Rolls	€12.00	€36.00
Wall Copings Single Sadle	Parrapet Wall	450x900mm	6	No.	€10.00	€60.00
Fibre cement board	cavity closer	6"	47	2.4m lgth	€6.00	€282.00
Meter box Inc Door	ESB		1	No.	€87.00	€87.00
Gable guides	timber frame		1		€100.00	€100.00

Materials Total	€45,601.21
------------------------	-------------------

Plant

Plant Needed	Hours/QTY	Hired off	Rate Per day	Rate per Hour/QTY	Fuel Cost	Total
Mixer	120			€1.50	€50.00	€180.00
Dumper 6T	0			€0.00		€0.00
Block Grab	0			€2.00		€0.00
3 Tonne Digger	0			€0.00		€0.00
Telehandler	80			€15.00	€100.00	€1,200.00
Acros	1			€50.00		€50.00
Delivery Charges	1			€200.00		€200.00

Plant Total	€1,630.00
--------------------	------------------


Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Superstructure blockwork	3	280		€35.00		€29,400.00
Stonework natural	3	110		€35.00		€11,550.00
Erect steel	2	5		€30.00		€300.00
Support precast slab	2	2		€30.00		€120.00
Grout precast slab	2	3		€30.00		€180.00
Gable guides (joiner)	2	2		€35.00		€140.00

Labour Total	€41,690.00
---------------------	-------------------

Assumptions:

Material	€45,601.21
Plant	€1,630.00
Labour	€41,690.00
Phase Total	€88,921.21



Client	Example Client	New Build
---------------	-----------------------	------------------

**Build Phase - Roof Structure and Finishes****Material**

Roof Structure	Description/Area	Size	QTY	In lengths of	Total Linear/M2	Cost per unit or L/Mtr	Total
Trusses (Decorative) PC SUM			4	1	4.00	€1,500.00	€6,000.00
Wall plate	treated/tanalised	4x3	29	4.8	139.20	€2.40	€334.08
Steel RSJ	Ridge	203x133x25UB	1	3.4	3.40	€45.00	€153.00
Steel RSJ	Ridge	305x102x33UB	1	13.3	13.30	€60.00	€798.00
Fire Coating Steel (Allowance)			1	1	1.00	€250.00	€250.00
Rafter	Main roof	6x2 C16	62	4.5	279.00	€3.05	€850.95
Rafter	Main roof outshot	6x2 C16	40	3.5	140.00	€3.05	€427.00
Valley Rafters		9x3	2	4.8	9.60	€7.90	€75.84
Ridge Board	All Ridge	9x2	9	4.8	43.20	€4.10	€177.12
Ceiling Joist	Utility/entrance/lobby	7x2	13	6.4	83.20	€4.40	€366.08
Flat roof joist		9x2	18	3.2	57.60	€4.10	€236.16
Ceiling Joist	First Floor	7x2	76	4.8	364.80	€3.50	€1,276.80
Ceiling Joist	porch	6x2	5	2.6	13.00	€3.10	€40.30
Collar Ties		6x2	12	3.2	38.40	€3.10	€119.04
Binders		4x2	5	4.8	24.00	€2.40	€57.60
Hangers		4x2	5	4.8	24.00	€1.05	€25.20
Struts		6x3	6	4.8	28.80	€5.30	€152.64
Lath Batons	fully graded	2x1	350	4.8	1,680.00	€0.85	€1,428.00
Fascia board		8x1	22	4.8	105.60	€2.85	€300.96
Furring Timber	Flat roof	6x2	6	4.8	28.80	€3.10	€89.28
Plywood Marine	Flat roof	2440x1220x18	7	1	7.00	€56.00	€392.00

Roof Coverings	Description	Size	QTY	Unit	Other	Cost per Unit	Total
Breathable Felt	Harcon	50 x 1.5m	0	rolls	€0.00	€0.00	€0.00
Breathable Felt	Tyvek Supro	50 x 1.5m	5	rolls	€0.00	€177.00	€885.00
Rafter Roll		6m roll	13	rolls	€0.00	€12.00	€156.00
Eaves Skirt		1.5m lengths	52	m	€0.00	€4.90	€254.80
Over fascia vents	10mm	1 m length	76	m	€0.00	€2.20	€167.20
Over fascia vents	25mm	1 m length	0	m	€0.00	€0.00	€0.00
Inline Slate Vent Glidevale	AV50			no.	€0.00		€0.00
Skylights inc flashing	Keylite	780 x 1180mm	6		€0.00	€425.00	€2,550.00
Fixings	Paslo nails	2"	2	pack of 1000	€0.00	€55.00	€110.00
Fixings	Paslo nails	3"	0	pack of 1000	€0.00	€0.00	€0.00
Fixings	Paslo nails	4"	2	pack of 1000	€0.00	€52.00	€104.00
Fixings	Galvanised nails	4"	1	5kg	€0.00	€0.00	€0.00
Fixings	Copper Nails	2"	14	box of 1000	€0.00	€52.00	€728.00
Fixings	Copper Nails	4"	0	box of 1000	€0.00	€0.00	€0.00
Fixings	Copper discs		0	box of 1000	€0.00	€0.00	€0.00
Fixings	Wall plate straps	600mm Straight	25	No.	€0.00	€2.40	€60.00
Fixings	Wall plate straps	600mm Twisted	55	No.	€0.00	€2.90	€159.50
Fixings	Wall plate straps	900mm Straight	0	No.	€0.00	€0.00	€0.00
Fixings	Wall plate straps	900mm Twisted	0	No.	€0.00	€0.00	€0.00
Fixings	Anchor bars		15	No.	€0.00	€2.00	€30.00
Fixings	M12 bolts		100	No.	€0.00	€5.10	€510.00
Fixings	Other	allowance	1		€0.00	€200.00	€200.00
Fixings	Metal joist hangers	single	0	No.	€0.00	€0.00	€0.00
Fixings	Metal joist hangers	double	0	No.	€0.00	€0.00	€0.00
Slate	natural	500x250	7000	No.	€0.00	€2.30	€16,100.00
Slate	manmade	500x250	0	No.	€0.00	€0.00	€0.00
Slate	natural	600x300	0	No.	€0.00	€0.00	€0.00
Slate	Man made	600x300	0	No.	€0.00	€0.00	€0.00
Concrete tiles	quinns flat	420x334	0	No.	€0.00	€0.90	€0.00
Clay tiles	snowdon	420x334	0	No.	€0.00	€0.00	€0.00
Ridge Caps	Tiles	400mm	0	No.	€0.00	€0.00	€0.00
Ridge Caps	Slates	400mm	110	No.	€0.00	€12.00	€1,320.00
Dry Ridge system			44	m	€0.00	€17.70	€778.80
Tile Vents				no.	€0.00	€0.00	€0.00
Slate Vents			12	no.	€0.00	€38.00	€456.00
Tile trim	Bent @ 20mm		16		€0.00	€20.00	€320.00
Slate trim			0		€0.00	€0.00	€0.00
Insulation	Flat roof	50mm	0	Sheets	€0.00	€0.00	€0.00
Insulation	Flat roof	100mm	0	Sheets	€0.00	€0.00	€0.00
Insulation	Flat roof	150mm	7	Sheets	€0.00	€65.00	€455.00
Lead Rolls	chimneys	6"	0	Rolls	€0.00	€0.00	€0.00
Lead Rolls	wall abutments	9"	1	Rolls	€0.00	€101.00	€101.00
Lead Rolls	chimneys	12"	0	Rolls	€0.00	€0.00	€0.00
Lead Rolls	valleys	18"	2	Rolls	€0.00	€194.00	€388.00
Specialised	Zinc		0	m2	€0.00	€0.00	€0.00
Specialised	EDPM		0	m2	€0.00	€0.00	€0.00
Specialised/flat roof/supply and fit	Trocal		18.8	m2	€0.00	€90.00	€1,692.00
Consumables	silicon/foam etc		0		€0.00	€0.00	€0.00
			0		€0.00	€0.00	€0.00

Materials Total	€34,741.27
------------------------	-------------------

Plant

Plant Needed	Description	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
Telehandler		32			€15.00	€85.00	€565.00
Delivery Charges		1			€120.00		€120.00

Plant Total	€685.00
--------------------	----------------

Labour


Task	Description	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Roof construction (joiner)		3	48		€28.00		€4,032.00
Tiler/slater		3	60		€28.00		€5,040.00
Flat roof construction		2	8		€28.00		€448.00
Flat roof finishes/as above		1	0.5		€0.50		€0.13
Leadwork/flashings		1	5		€28.00		€140.00
Erect steel RSJs/wooden purlins		2	4		€28.00		€224.00
Soffit/Fascia frame		2	8		€28.00		€448.00
Housekeeping		1	4		€28.00		€112.00

Refer to final breakdown for PVC soffit, fascia & guttering

Labour Total	€10,444.13
---------------------	-------------------

Assumptions:

Material	€34,741.27
Plant	€685.00
Labour	€10,444.13
Phase Total	€45,870.40

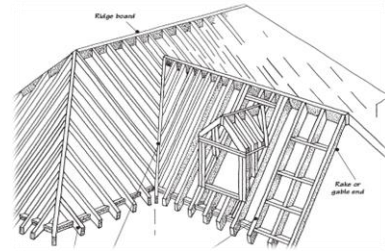

Client	Example Client	New Build
---------------	-----------------------	------------------

**Build Phase - First Fix Joinery****Material**

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Timber	Wall Studding	4x2	5	m	€ 2.30	€ 11.50
Door Frame		5 1/4" x 1 1/4"	105	m	€ 4.30	€ 451.50
Plasterboard	Ceilings	8 x 4 x 12.5mm	10	sheets	€ 12.25	€ 122.50
Plasterboard Vaulted ceiling	Insulated	50mm + 12.5mm	15	sheets	€ 54.90	€ 823.50
Plasterboard Flat ceiling	Insulated	50mm + 12.5mm	50	sheets	€ 54.90	€ 2,745.00
Kingspan TF70/TP10 Rafter Insulation	2.4x1.2m vaulted	125mm	15	sheets	€ 88.00	€ 1,320.00
Insulation Loft Roll	Isover G3 Spacesaver	200mm (6.03m2)	24	Rolls	€ 59.00	€ 1,416.00
Vario KM Duplex UV Smart Membrane	1.5x40m		1	Rolls	€ 235.00	€ 235.00
Fixings	Chipboard screw	5x100mm	2	box of 200	€ 18.90	€ 37.80
Fixings	insulated p/b fixings		2	Number	€ 50.00	€ 100.00
Fixings	Other/Allowance		1		€ 100.00	€ 100.00
Suspended Ceiling	Metal supply & fit		105	m2	€ 20.00	€ 2,100.00

Materials Total	€ 9,462.80
------------------------	-------------------

Plant

Plant Needed	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
Delivery Charges	1			€85.00		€85.00

Plant Total	€85.00
--------------------	---------------


Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Stud walls	2	4		€30.00		€240.00
Rafter insulation	2	8		€30.00		€480.00
Loft insulation	2	8		€30.00		€480.00
Door frames	2	12		€30.00		€720.00
Plasterboarding/all	2	24		€30.00		€1,440.00
Air Tight Membrane	2	20		€30.00		€1,200.00

Labour Total	€4,560.00
---------------------	------------------

Assumptions:

Material	€9,462.80
Plant	€85.00
Labour	€4,560.00
Phase Total	€14,107.80

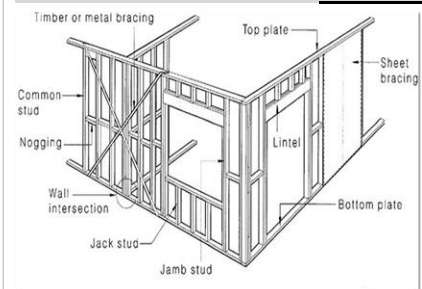

Client**Example Client****New Build****Build Phase - Plastering****Material**

Material	Description/Area	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Sand	External walls		16	tonne	€ 25.00	€ 400.00
Sand	Internal walls		18	tonne	€ 25.00	€ 450.00
Cement	External walls	25kg	48	bags	€ 6.60	€ 316.80
Cement	Internal walls	25kg	130	bags	€ 6.60	€ 858.00
Limestone Chips/Dash	External walls	25kg	25	bags	€ 6.60	€ 165.00
Lime		25kg	25	bags	€ 10.15	€ 253.75
Waterproofer	Cementone	5 litres	1	litres	€ 15.00	€ 15.00
Skim Finish	Internal walls	25kg	110	bags	€ 12.50	€ 1,375.00
Bonding	bonding carlite		6	bags	€ 20.65	€ 123.90
Scrim Cloth	3" Self adhesive		2	rolls	€ 7.50	€ 15.00
Corner Beading	Fine		25		€ 2.20	€ 55.00
	Heavy		30		€ 2.60	€ 78.00
Fixings	general allowance		1		€ 50.00	€ 50.00

Materials Total	€ 4,155.45
------------------------	-------------------

Plant

Plant Needed	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
Mixer	80			€1.50	€30.00	€150.00
Telehandler	24			€15.00	€70.00	€430.00
Delivery Charges	1			€0.00	€120.00	€120.00

Plant Total	€700.00
--------------------	----------------

Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Plastering (sub out)	3	300		€30.00		€27,000.00
Housekeeping	2	4		€30.00		€240.00

Labour Total	€27,240.00
---------------------	-------------------

Assumptions:

Material	€4,155.45
Plant	€700.00
Labour	€27,240.00
Phase Total	€32,095.45



Client Example Client **New Build**



Build Phase - Finish floor

Material

Material	Description/Area	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Polythene	25x4m	1200g	3	roll	€ 35.00	€ 105.00
Insulation	Ground floor	50mm	37	sheets	€ 31.00	€ 1,147.00
Insulation	Ground floor	150mm	75	sheets	€ 80.20	€ 6,015.00
Expansion		15m	5	rolls	€ 30.00	€ 150.00
Screed	sand/cement		24	m3	€ 126.00	€ 3,024.00
Fixings			1		€ 30.00	€ 30.00

Materials Total € 10,471.00

Plant

Plant Needed	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
Delivery Charges	1				€85.00	€85.00

Plant Total €85.00


Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Floor prep	2	8		€25.00		€400.00
Lay insulation/polythene	2	16		€25.00		€800.00
Pour finish floor 314m2	4	20		€30.00		€2,400.00

Labour Total €3,600.00

Assumptions:

Material	€10,471.00
Plant	€85.00
Labour	€3,600.00
Phase Total	€14,156.00

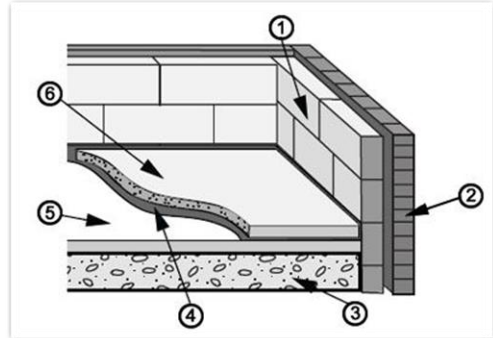

Client Example Client **New Build**



Build Phase - Trim out

Material

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Doors	Standard		16	number of	€ 165.00	€ 2,640.00
Doors	BI Fold	Allowance	6	number of	€ 135.00	€ 810.00
Door Stop	Full	100 x 12	78	m	€ 3.00	€ 234.00
Skirting	Standard mdf	150 x 19	365	m	€ 4.58	€ 1,671.70
Architrave	Standard mdf	69 x 19mm	165	m	€ 4.00	€ 660.00
Ironmongery	handles/hinges		16	allowance per door	€ 55.00	€ 880.00
Window board	mdf	19mm	40	m	€ 9.00	€ 360.00
Hotpress/Shelving	timber	2x1 planed	50	m	€ 1.25	€ 62.50
Fixings	allowance		1		€ 125.00	€ 125.00
Adhesives			1		€ 20.00	€ 20.00

Materials Total € 8,318.20

Plant

Plant Needed	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
Delivery Charges	1			€85.00	€0.00	€85.00

Plant Total €85.00


Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Fit doors/swing/hang	2	30		€30.00		€1,800.00
Fit ironmongery	1	20		€30.00		€600.00
Fit skirting/architrave	2	24		€30.00		€1,440.00
Shelving/Units	1	8		€30.00		€240.00
Window Board	1	8		€30.00		€240.00
Hot press	1	6		€30.00		€180.00
Boxing of pipes	1	4		€30.00		€120.00

Labour Total €4,620.00

Assumptions:

Material	€8,318.20
Plant	€85.00
Labour	€4,620.00
Phase Total	€13,023.20

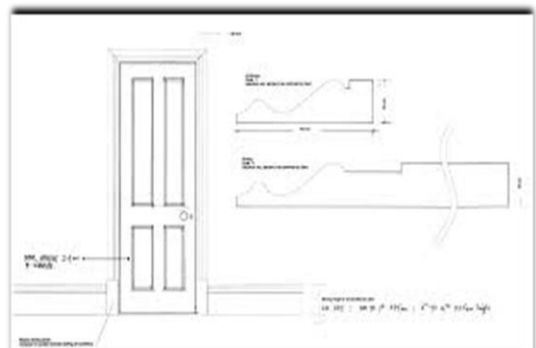

Client	Example Client	New Build
---------------	-----------------------	------------------

**Build Phase - Sewers/Drainage****Material**

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Stone / Aggregate	Crusher Run	3"	20	Tonne	€ 12.50	€250.00
Stone / Aggregate	Drainage rough sand		30	Tonne	€ 18.00	€540.00
Stone / Aggregate	Drainage Stone	1/4"	60	Tonne	€ 15.00	€900.00
Stone / Aggregate		Dust	12	Tonne	€ 14.00	€168.00
Concrete	fit treatment plant	15N	3	Mc3	€ 100.00	€300.00
Pipes	Sewer Pipe 6m	4"	21	lengths	€ 26.00	€546.00
Pipes	Storm Pipe 6m	4"	18	lengths	€ 26.00	€468.00
Treatment plant	Sewer treatment	6 person	1	number	€ 6,500.00	€6,500.00
Fittings	Storm Gullies	4" fittings	13	number	€ 28.00	€364.00
Fittings	Roddable BIG gully		5	number	€ 29.00	€145.00
Fittings	460/18" man hole base		8	number	€ 37.00	€296.00
Fittings	460 manhole riser		16	number	€ 25.00	€400.00
Fittings	460 polypropylene cover		8	number	€ 35.50	€284.00
Fittings	320/12" manhole base		8	number	€ 31.00	€248.00
Fittings	320/12" manhole riser		16	number	€ 14.00	€224.00
Fittings	320 polypropylene cover		8	number	€ 51.00	€408.00
Fittings	Pipe cover vents		3	number	€ 8.00	€24.00
Fittings	Rodeyes	Galv	2	number	€ 35.00	€70.00
Fittings	15°	4"	3	number	€ 4.00	€12.00
Fittings	30°	4"	4	number	€ 4.00	€16.00
Fittings	45°	4"	5	number	€ 4.00	€20.00
Fittings	L/R 90°	4"	5	number	€ 18.00	€90.00
Fittings	T's	4"	4	number	€ 8.00	€32.00
Fittings	Y's	4"	4	number	€ 8.00	€32.00
Fittings	15°	4"	4	number	€ 4.00	€16.00
Fittings	30°	4"	4	number	€ 4.00	€16.00
Fittings	45°	4"	4	number	€ 4.00	€16.00
Fittings	T's	4"	3	number	€ 8.00	€24.00
Fittings	Y's	4"	3	number	€ 8.00	€24.00
Ducting	Black Ducting	2"	4		€ 16.00	€64.00
Land Drain	100m	50 roll	2		€ 56.00	€112.00
Power cable	to treatment plant		1		€ 250.00	€250.00
ESB ducting	6m lengths	4"/110mm	6		€ 45.00	€270.00
Water pipe fittings	Allowance		1		€ 125.00	€125.00
Grey ducting	Eircom	50mm	4		€ 18.00	€72.00
Water pipe	Blue alkaline	25mmx50mtr	1		€ 85.00	€85.00

Materials Total	€13,411.00
------------------------	-------------------

Plant

Plant Needed	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
6 ton digger	0			€0.00	€ 0.00	€0.00
Dumper 6T	40			€12.00	€ 120.00	€600.00
13 ton digger	40			€55.00	€ 0.00	€2,200.00
lorry hire	0			€0.00	€ 0.00	€0.00
3 ton digger	0			€0.00	€ 0.00	€0.00
Delivery Charges	1			€150.00	€ 0.00	€150.00
Small plant allowance	1			€95.00	€ 25.00	€120.00

Plant Total	€3,070.00
--------------------	------------------


Labour

Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Drainage/Percolation	2	18		€25.00		€900.00
Sewers/lay	2	16		€25.00		€800.00
Treatment plant	2	6		€25.00		€300.00
Backfilling of trenches	1	3		€25.00		€75.00
Sewer snagging	1	3		€25.00		€75.00
Housekeeping	1	2		€25.00		€50.00

Labour Total	€2,200.00
---------------------	------------------

Assumptions:

Material	€13,411.00
Plant	€3,070.00
Labour	€2,200.00
Phase Total	€18,681.00

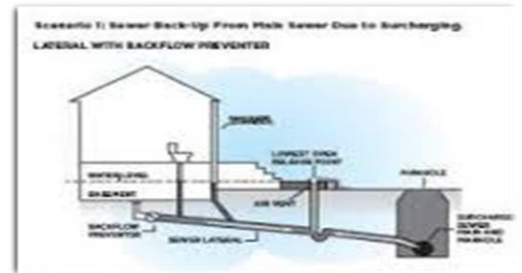

Client Example Client **New Build**



Build Phase - Street/Footpaths Prep

Material

Material	Description	Size	Quantity	Unit of Meas	Cost per Unit	Total Cost
Concrete/fine mix	footpaths/steps	30N	14	mc3	€112.00	€1,568.00
Tarmac/Allowance/sma			604	m2	€22.00	€13,288.00
Aggregates	Crusher run	2"	60	tonne	€12.50	€750.00
Aggregates	Blinding		40	tonne	€14.00	€560.00
Aggregates	Dust		3	tonne	€15.00	€45.00

Materials Total €16,211.00

Plant

Plant Needed	Hours	Hired off	Rate Per day	Rate per Hour	Fuel Cost	Total
13 T Digger	16		€0.00	€60.00	€0.00	€960.00
Dumper 6T	16		€0.00	€10.00	€45.00	€205.00
Dumper 9T	0		€0.00	€0.00	€0.00	€0.00
Tractor & dump	0		€0.00	€0.00	€0.00	€0.00
Telehandler	0		€0.00	€0.00	€0.00	€0.00
Delivery Charges	1		€0.00	€125.00	€0.00	€125.00

Plant Total €1,290.00

Labour


Task	Operatives	Hours on task	Rate per day	Rate per hour	Other	Total
Footpath shutter prep	2	8		€25.00		€400.00
Stone up footpath & street	2	12		€25.00		€600.00
Form and build steps	2	4		€25.00		€200.00
Prep for tarring	2	8		€25.00		€400.00

Labour Total €1,600.00

Assumptions:

Material	€16,211.00
Plant	€1,290.00
Labour	€1,600.00
Phase Total	€19,101.00

Cross-Section of a Driveway/Pathway



Client Example Client



Build Phase Breakdown


Build Phase	Material cost	Plant cost	Labour Cost	Other	Total Cost
Preliminaries/at Clients descreation	€17,012.00				€17,012.00
Site Clearance	€5,959.00	€3,354.00	€1,770.48		€11,083.48
Foundations	€17,504.50	€1,018.00	€3,510.25		€22,032.75
Substructure	€2,594.75	€262.00	€1,260.00		€4,116.75
Overslab	€2,172.50	€1,205.00	€450.00		€3,827.50
Superstructure	€45,601.21	€1,630.00	€41,690.00		€88,921.21
Roof Structure & Finishes	€34,741.27	€685.00	€10,444.14		€45,870.41
PVC Soffit/Guttering	PC Sum			€2,650.00	€2,650.00
External Windows/Doors	PC Sum			€34,000.00	€34,000.00
1st Fix Joinery	€9,462.80	€85.00	€4,560.00		€14,107.80
Plastering	€4,155.45	€700.00	€27,240.00		€32,095.45
Finish floor	€10,471.00	€85.00	€3,600.00		€14,156.00
Plumbing	PC Sum			€35,000.00	€35,000.00
Electrical/Solar panels	PC Sum			€18,000.00	€18,000.00
Trim out	€8,318.20	€85.00	€4,620.00		€13,023.20
Streets/Paving/Footpath	€16,211.00	€1,290.00	€1,600.00		€19,101.00
Sewers & Services	€13,411.00	€3,070.00	€2,200.00		€18,681.00
Kitchen	PC Sum			€20,000.00	€20,000.00
Fireplace/stove	PC Sum			€2,000.00	€2,000.00
Sanitary ware	PC Sum			€6,000.00	€6,000.00
Stairs	PC Sum			€6,500.00	€6,500.00

Total	€187,614.68	€13,469.00	€102,944.87	€124,150.00	€428,178.55
--------------	--------------------	-------------------	--------------------	--------------------	--------------------

Total Self Build Price € 428,178.55

*PC sums noted in

* Preliminaries relate to general set up of the site, scaffolding, skip hire and security fencing if required

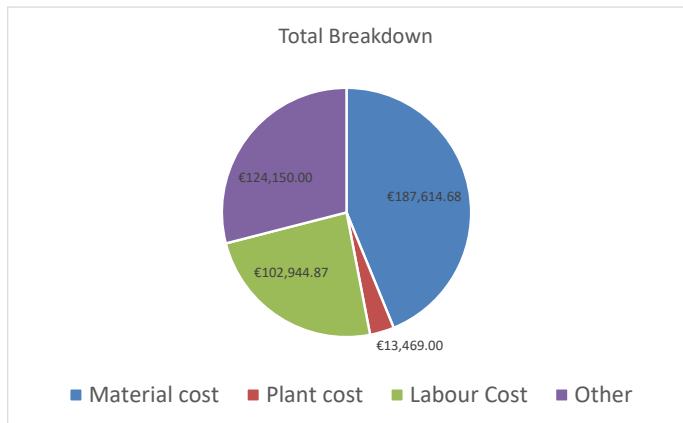

Terms & Conditions

If little or no specification is available and assumptions are made, this needs to be checked with your architect before any works commence.

We aim to complete full estimations within 5-10 working days. This may increase during busy periods or bank holidays.

If you have selected for an express report to be done, we aim to complete this in 2-5 working days

50% deposit required on full estimations. Balance due on completion of report.
Reports cannot be released until full payment has been received

If a client wishes to cancel once deposit has been made, deposit is non refundable.

Due to the nature of electrics and plumbing being so variable we will provide PC sums for them, unless client or architect advises of a specific figure.

Price lists for general materials in the report will be based on hardware store/builders merchant prices withing a 40/50 mile radius

Specific items like rooflights, windows/doors, stone, pre-stressed slab etc will be sent out for pricing and quotations will be attached to the final report

Any typing or clerical errors on reports will be rectified Free of Charge

If changes are made to the plans or specification and the client would like the report revised, this will be subject to a revision fee

Reports are emailed in PDF once completed. We do not post reports

If clients would like a copy of their drawings printed to scale, we offer this as an additional service. £1.50/€2.00 per page
